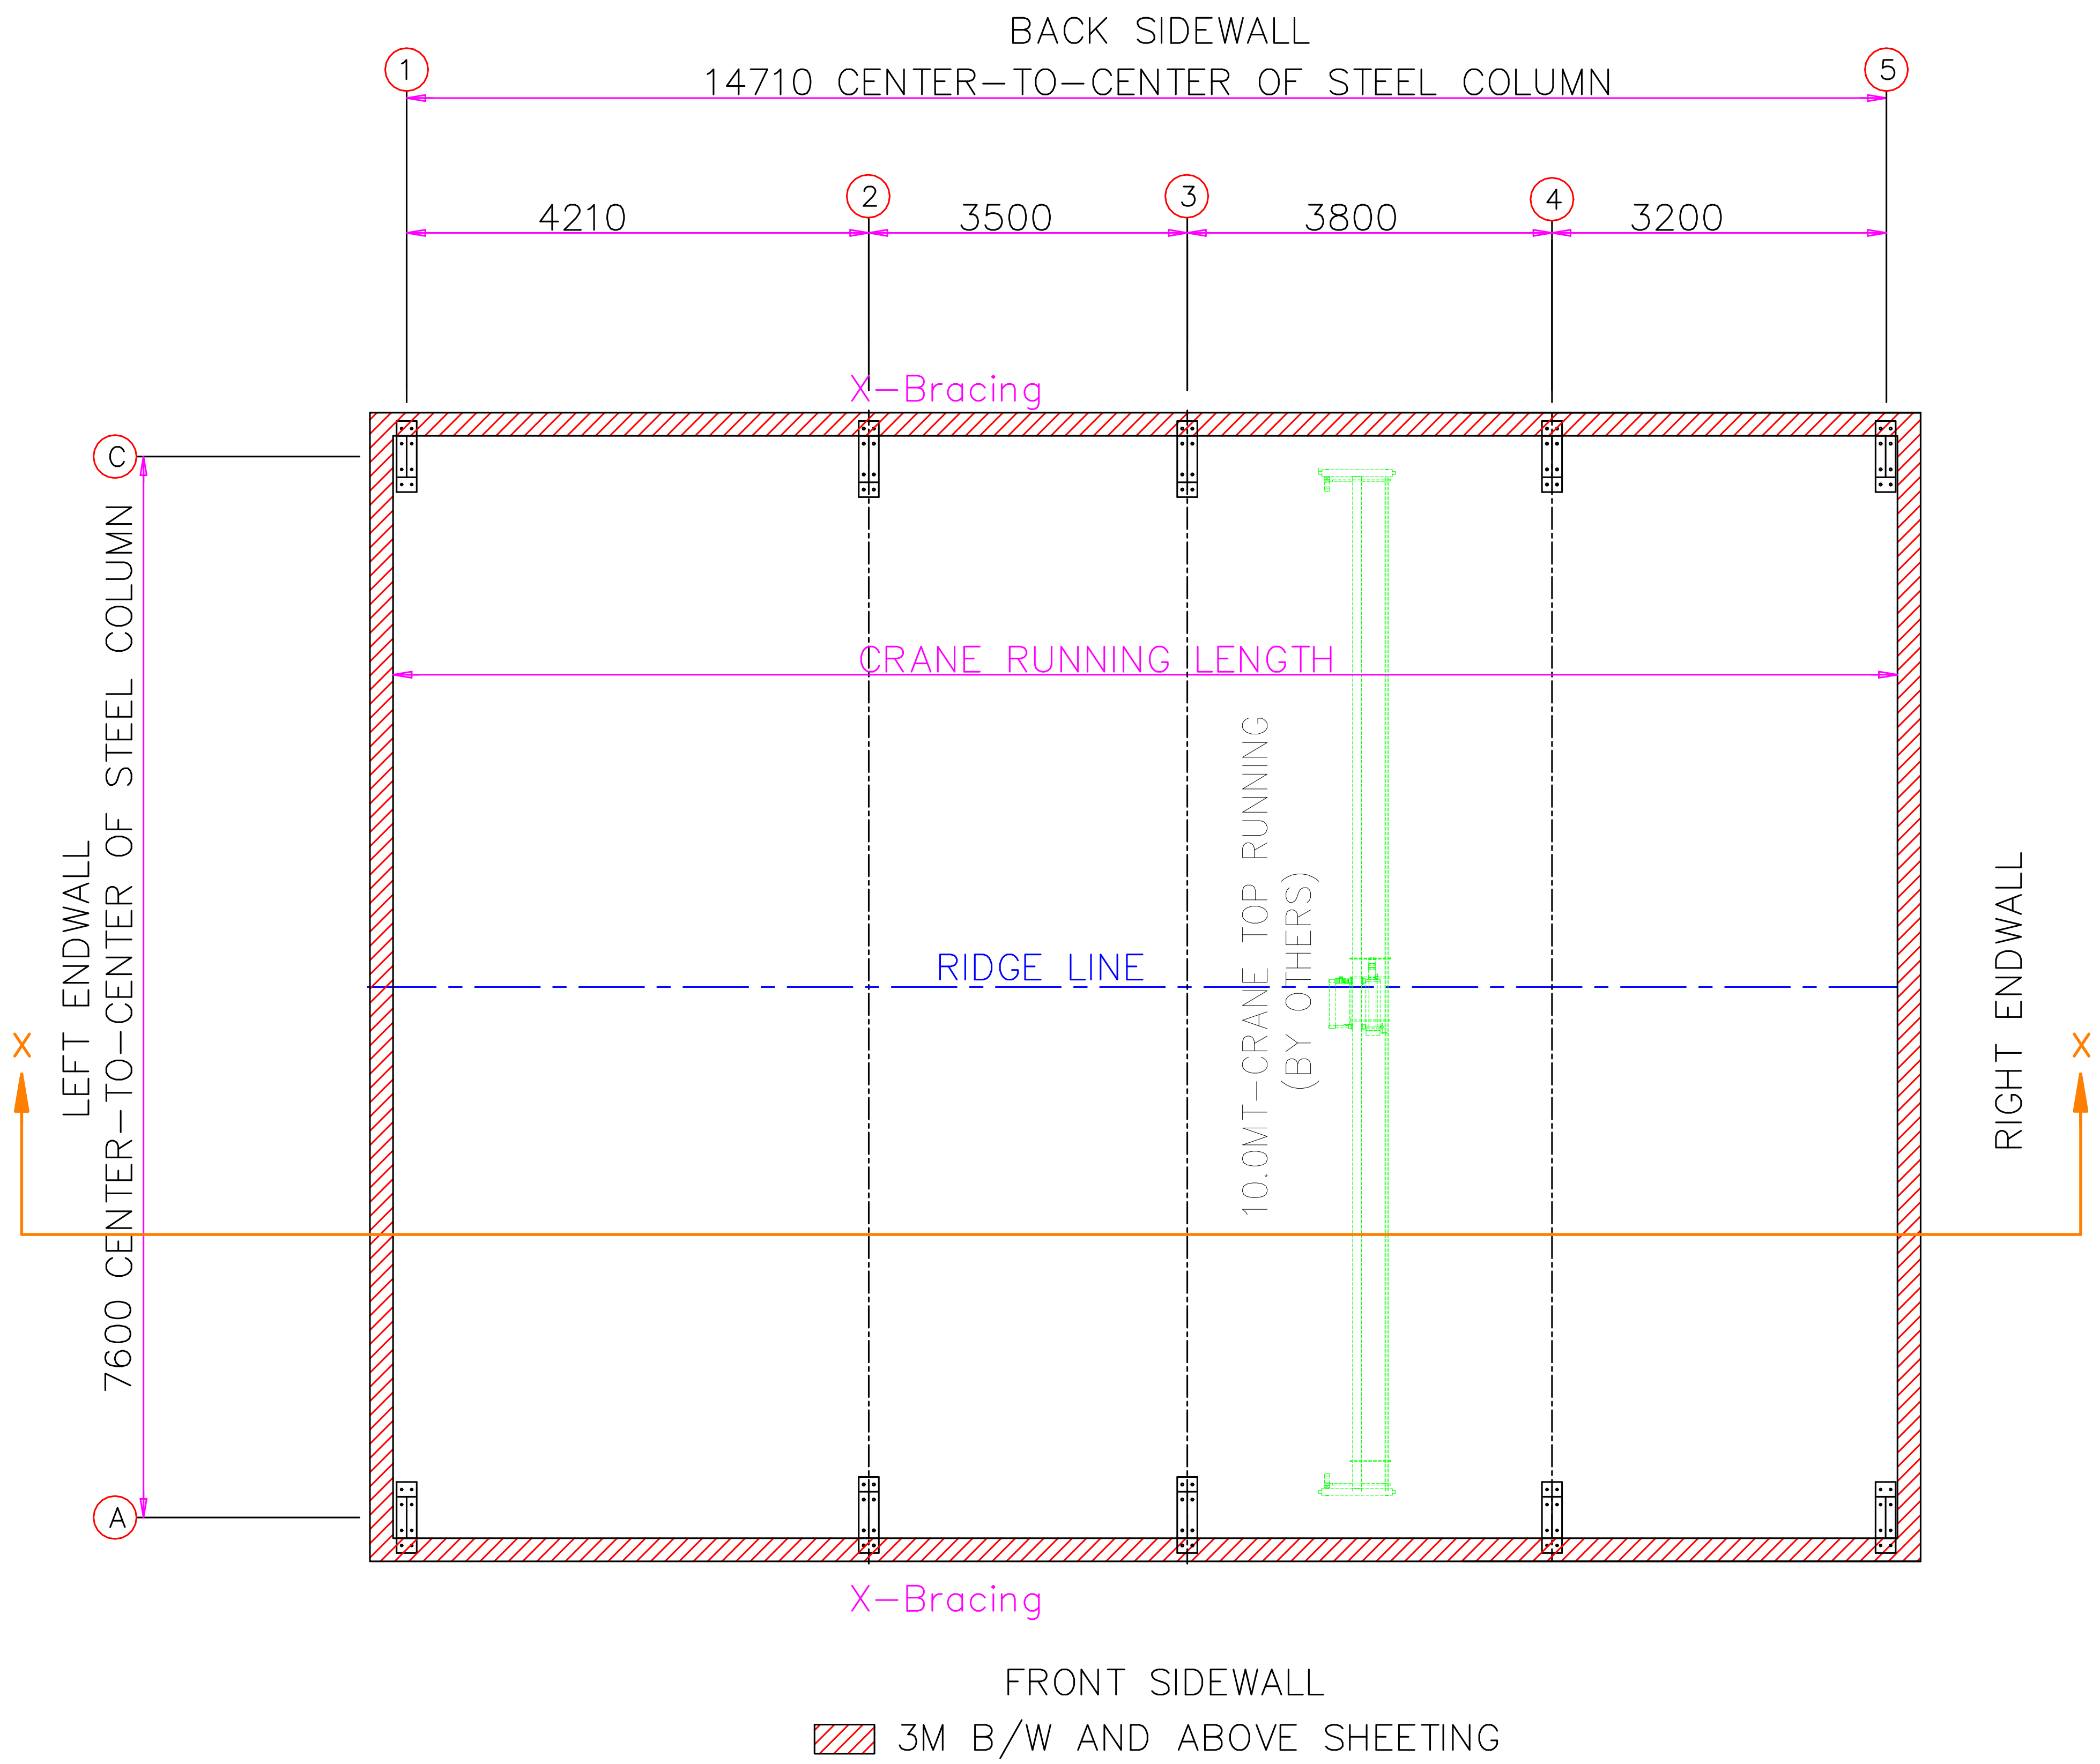

PROPOSED PLAN

NOTE: All Base Plates @ 0 (U.N.)

INFINITI SOLUTIONS				
PROJECT	SHED	PROPOSED PLAN		
ID	C187-119	DESIGN: DRS	DRAFT: HJB	CHECK: DRS
PROJECT ADDRESS	MUMBAI	DATE: 11/03/2026		

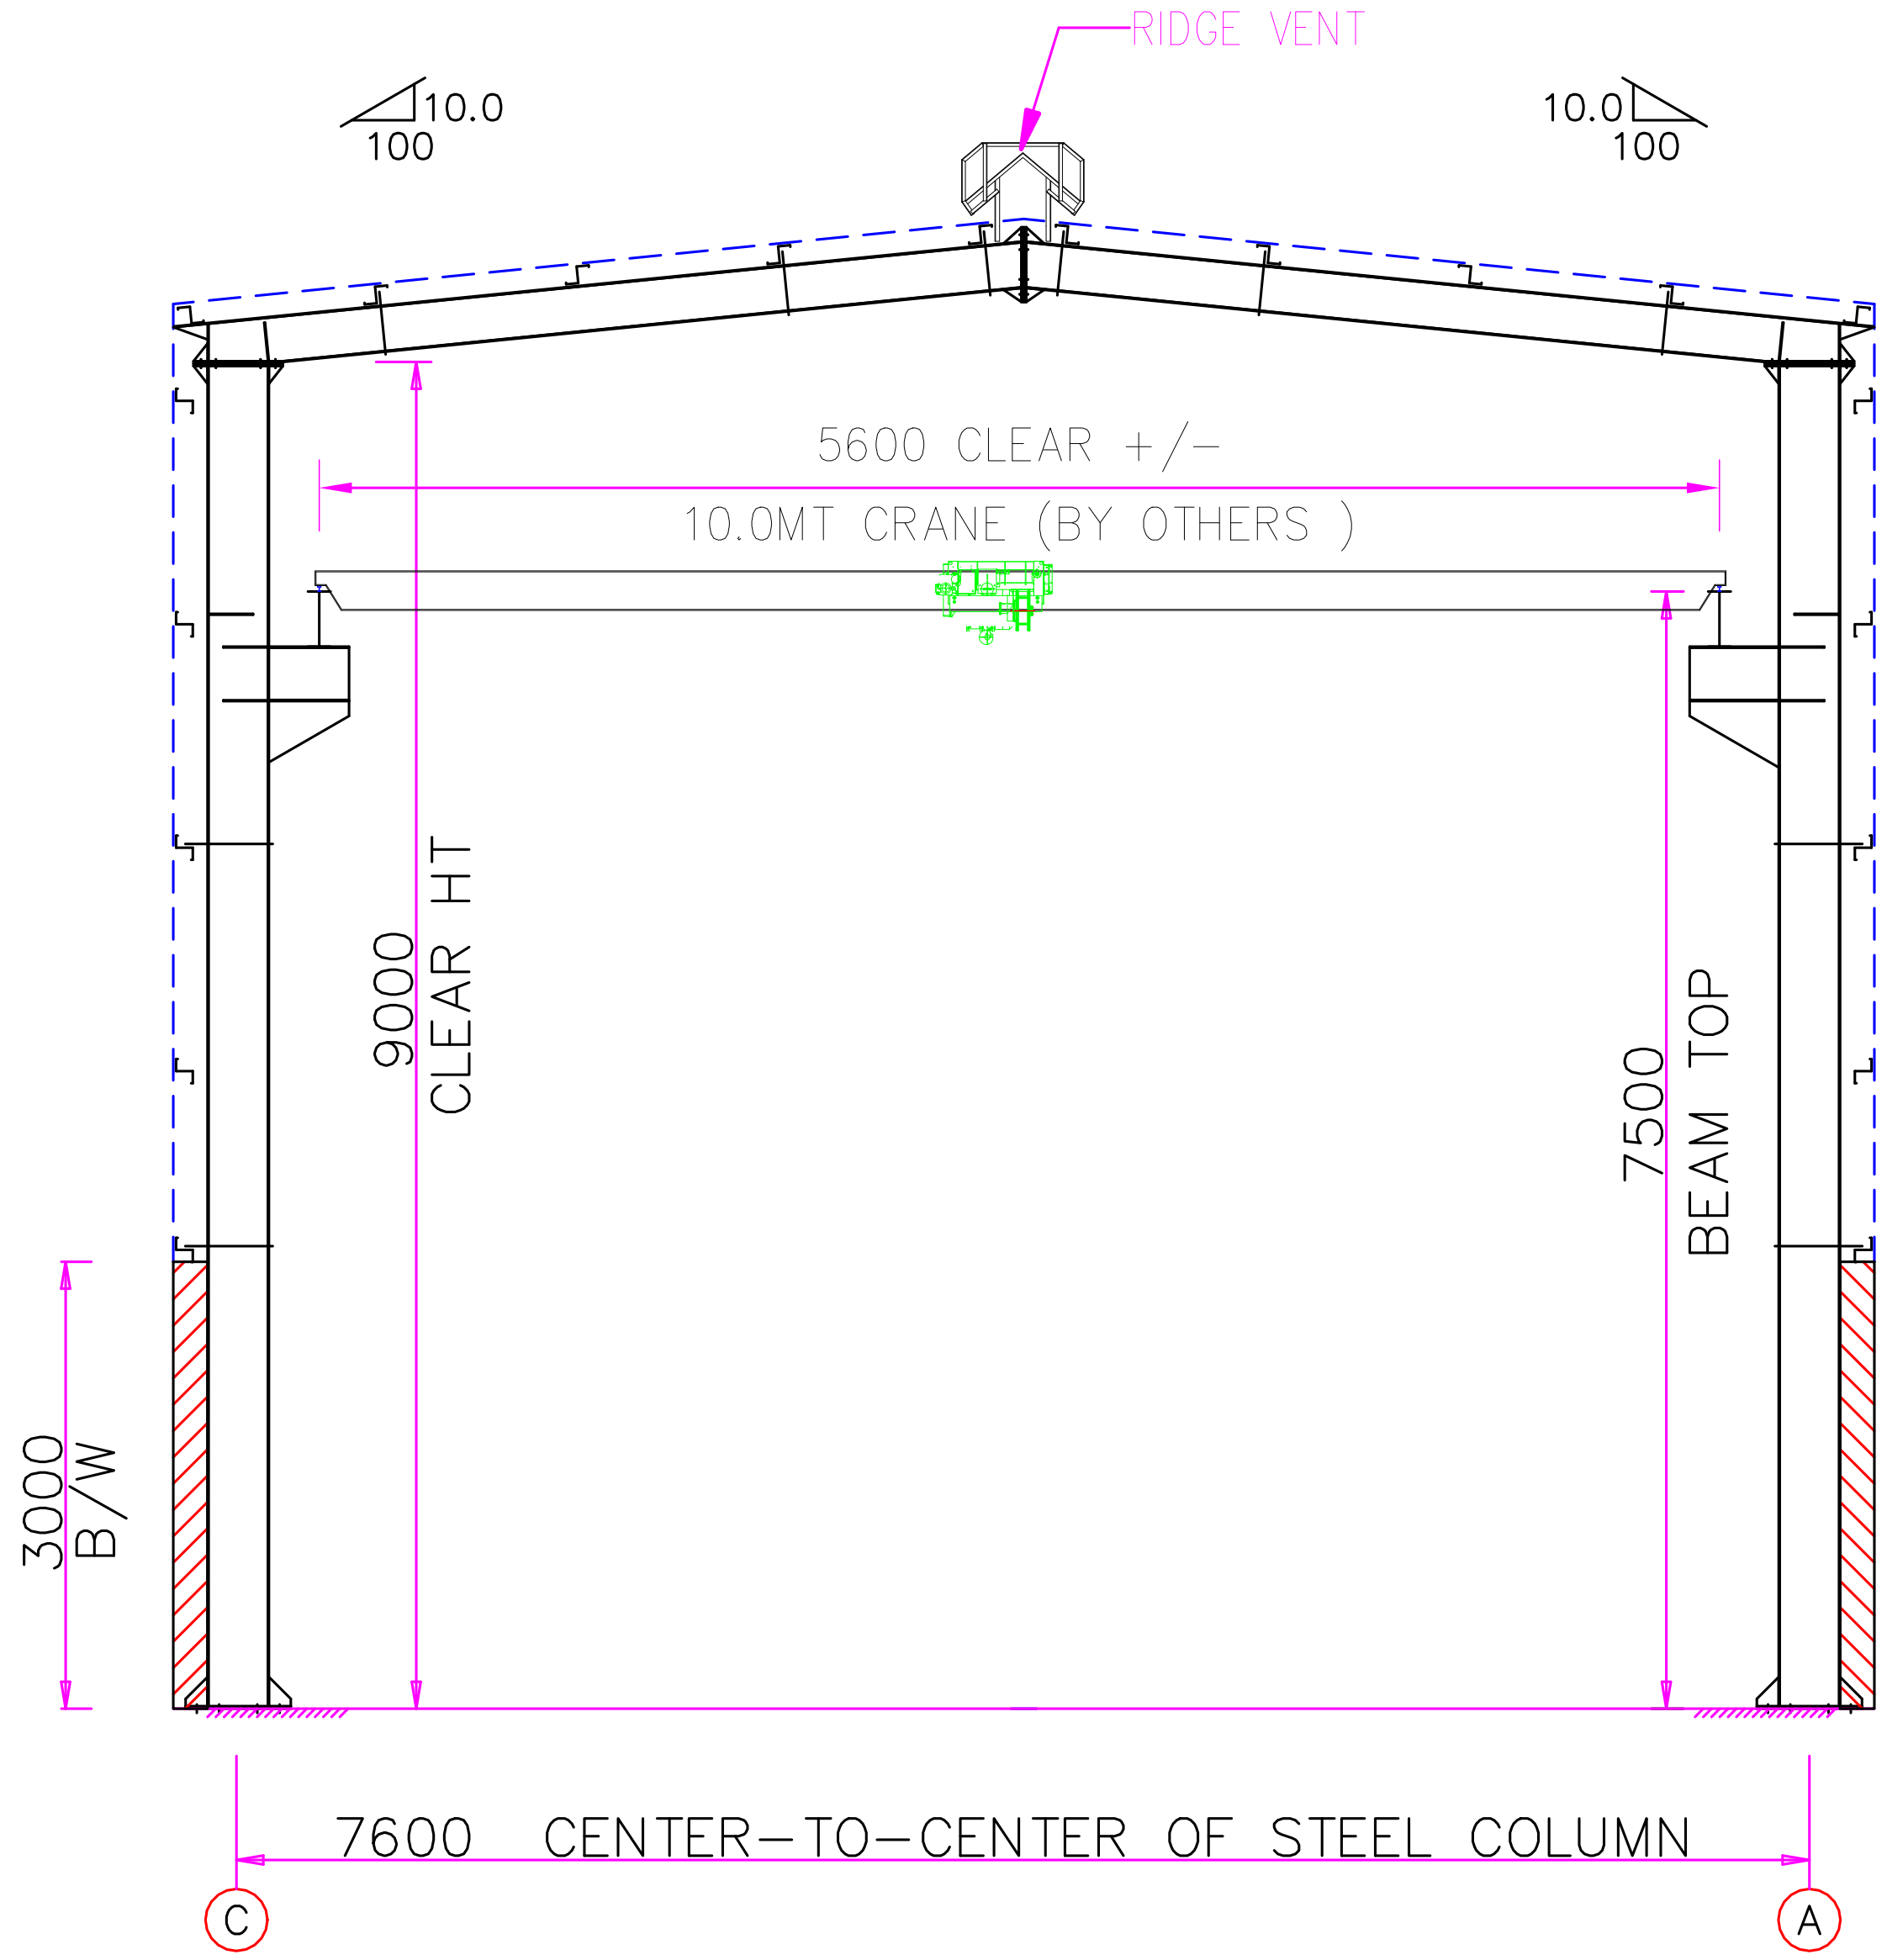

RIGID FRAME ELEVATION: FRAME LINE 2 3

INFINITI SOLUTIONS				
PROJECT	SHED	RIGID FRAME ELEVATION		
ID	C187−119	DESIGN: DRS	DRAFT: HJB	CHECK: DRS
PROJECT ADDRESS	MUMBAI	DATE: 11/03/2026		

OUTLINE SPECIFICATIONS

Date	11-03-2026	Client		Project Location	Mumbai				
Proposal Id	C187-119-R3	Project		Building No.	1	Option	1	Revision	4

Sr.No.	Description	PEB SPECIFICATIONS			
1.	**Building type**	Clear span		**Area in m^2**	115
2.	**Length in m (c/c of steel column)**	14.710		**Length wise bay spacing**	1@4.21+1@3.5+1@3.8+1@3.2
3.	**Width in m (c/c of steel column)**	7.6		**End wall column spacing**	1@7.6
4.	**Width modules in m**	1@7.6	NA	**No. of interior columns per frame**	0
5.	**Clear height in m**	9		**Frames symmetrical**	Yes
6.	**Roof**	**Slope:** 10:100	**Cladding:** 0.5 mm Double skin roofing panels	**Rainwater drainage:** Eave Gutters and Down spouts	
7.	**Future Expansion**	NA			
8.	**Block Wall**	All around 3 m height block wall; bypass condition, wall width 230mm			
9.	**Column base elevations**	NA (At FFL)			
10.	**Wall Cladding**	Puff panels above block wall			
11.	**Insulation**	Roof: fiber glass insulation	Outer Walls: Insulated Sandwich Panel	Partition walls: NA	
12.	**Openings**	(see below)			
13.	**Extensions**	Eave: NA	Gable: NA	Canopies: (see below)	Parapet: NA
14.	**Accessories**	(see below)			Any other: NA

12. Openings

Outer side only	Numbers	Type	Size in m (w x h)
Doors	NA		
Windows	NA		

Location of doors & bracing

Side Wall Gridlines	1-2	2-3	3-4	4-5	Right End Wall
Front Side Wall		X			
Back Side Wall		X			

End Wall Axes	A-B	B-C	Back Side Wall
Right End Wall			
Left End Wall			

13. Extensions – Canopies:

Extension in m: NA	Location: Above RUDs
Clear height in m: NA	Rainwater drainage: NA
Slope: NA	Soffit panels: NA

14. Accessories

Wall Lights:	NA	Roof Monitor	NA
Skylights:	NA	Cage ladder	NA
Turbo Ventilators:	NA	Ridge Ventilators:	Yes

15.	**Crane**	Crane Capacity in MT: 10 Crane beam top height in m: 7.5 Crane span in m: 6.8 +/- Crane running length in m: 14.71 Crane class: II (Normal duty)	Crane Type: Top running Type of Girder: Single Walkway / Service platform: NA Monkey ladder: NA	Bridge Weight in MT: 5.2 Hoist/Trolley Weight in MT: 1.2 Number of Wheels: Wheel Load in MT: 6.2 Wheel Base in mm: 1900
16.	**Mezzanine**	NA		
17.	**Partition Walls**	NA		

DESIGN CONSIDERATIONS

18. For Frames	DESIGN LOADS		LOCATION - CLIMATIC DATA		SERVICEBILITY CRITERIA	
(Standard codes and manuals used in design – IS 800 2007, IS 875-Part -III, IS 801, IS 1893 Part 2016)	Dead Load in kN/m^2	0.15	Max wind speed in m/s	**44**	Frames	H/100, L/180
	Live Load in kN/m^2	0.75	Exposure category	B	Purlins	Span/150
	Collateral load in kN/m^2	NA	Max rainfall intensity in mm/hr	150	Girts	Span/150
	Any other	NA	Seismic Design category (Coefficient)	III (0.16)	Crane Beams	Span/750
Design Software: Staad			Max Temperature variation in °C	20	Mezzanine Beams	Span/240

19.	**Assumptions & Remarks**	*Built-up sections are made from hot rolled plates conforming to ASTM A-572 Gr50 (345MPa) steel.* *The plates are joined together with double side welding. Sections consist of minimum 5mm for flange & minimum 4mm for web thickness.* *Cold formed sections thickness 1.5 mm or more are made of hot rolled sheet of Gr50 (345 MPa) steel.* *Primary structural connections are high strength machine bolts conforming to ASTM A325 or equivalent.* *Sheeting profile considered is of 1 m standard width, formed from a coil of 1.220 m. Single colour sheeting of up to maximum 9 m lengths is considered.* **Not considered in scope:** *Foundation, Block wall (Civil work). Crane Bridge, Trolley, Rail and its installation.*
20.	**Key Design considerations**	*1. For wind calculation Terrain category is considered as per IS 875 Part – III, 2015 is considered.* *2. Internal coefficient is 0.2+/- is considered for wind calculation.* *3. All main frame columns are considered as Fixed base; rest end wall columns are pinned base.* *4. Tube Bracing at Roof & tube bracing @ walls considered* ***5. Abus crane data is considered for design. The customer must provide the crane data before final design.***
21.	**Instructions (if any)**	
